

GREAT THINGS ARE HAPPENING IN PARAMOUNT SCHOOLS



Facilities Projects Update October 2017

Dr. Ruth Perez, Superintendent Ruben Frutos, Asst. Supt., Business Services Scott Law, Director - Facilities and Planning

CURRENT PROCESSES – STEPS:

- Partner agencies moves P3 and Pathways
- Project accounting systems and new fund
- Finalizing plans and begin architectural design

NEXT STEPS:

- Board review and approval
- Submittal to DSA, Bid process
- Contract award, Construction





DSA PROCESS – STEPS

- Plans and architectural design
- Board design review and approval
- Submittal to DSA
 - Current "Bin" time Approx. 6 months
 - (In some cases, the DSA approval process moves project components to next year) – To alleviate delays, we have split projects in to phases that can be independently approved.
- Bid process
- Contract award, Construction





FACILITIES PROJECTS UPDATE

<u>Current Process</u>: Planning, development and implementation of the following projects:

- 1. Collins demo project
- 2. PHS West campus renovation
 - 1. Exterior hallways
 - 2. Interior hallways
 - 3. Windows
 - 4. Entry Lobby
- 3. CDS paint and fencing
- 4. P3 Clinic and Pathways
- 5. Odyssey STEM Academy
- Tanner school



PREPARING STUDENTS FOR COLLEGE AND CAREERS

FACILITIES PROJECTS UPDATE











Collins Portable Demo

CDS Paint Project

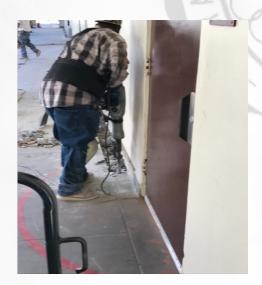

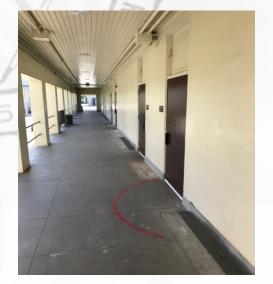

PHS West concrete removal and paint



PREPARING STUDENTS FOR COLLEGE AND CAREERS









Collins drainage system upgrades









PHS West hallway floor, wall and lighting remodel




PREPARING STUDENTS FOR COLLEGE AND CAREERS







PHS West lobby entry improvements










PREPARING STUDENTS FOR COLLEGE AND CAREERS









P3 Clinic at Wirtz campus









PHS West window replacement project



PARAMOUNT UNIFIED SCHOOL DISTRICT PREPARING STUDENTS FOR COLLEGE AND CAREERS

Modular Buildings



	SIZE	MODEL	DELIVERED TO	ADD/REPLACE	DELIVERY TIMELINE	XISTING SITE BUILDIN
1st Delivery	24X60	MOD TECH	Collins	Replace	Delivered	Hold
	24X60	MOD TECH	Collins	Replace	Delivered	Hold
	24X60	MOD TECH	Collins	Replace	Delivered	Hold
	24X60	MOD TECH	Collins	Replace	Delivered	Hold
	24X60	MOD TECH	Collins	Replace	Delivered	Hold
	24X60	MOD TECH	Collins	Replace	Delivered	Hold
2nd Delivery	24x60	MOD TECH	Mokler	Replace	Delivered	Demo
	12X40	MOD TECH	Roosevelt	Replace	Delivered	Sale
	24X60		Collins	Replace	Delivered	Hold
	24X60		Collins	Replace	Delivered	Hold
3rd Delivery	24X60	MOD TECH	Buena Vista	Add Portable (replace displaced Lakewood occupancy	Delivered	Add
	24X60	MOD TECH	Wirtz	Add Portable (replace displaced program due to P3)	Delivered	Add
	24X60	MOD TECH	Zamboni	Add Band Room	Delivered	Add
	24X40	MOD TECH	Gaines	Replace DOH building	Delivered	Demo
	24X40	MOD TECH	Gaines	Replace DOH Building	Delivered	Demo
	24X40	MOD TECH	Los Cerritos	Replace DOH Building	Delivered	Sale
	12X40	MOD TECH	Collins	add restroom capacity - Kinder (or Pathways)	Delivered	Add
	24X40		Alondra	Add Band Room	Delivered	Add



PREPARING STUDENTS FOR COLLEGE AND CAREERS



Paramount USD

BOND FACILITIES PROJECTS SEQUENCE LIST

March 13, 2017

Board Facilities Bond Project Review and Selection

				Board Facilities Bond Project Review and Selection			
Proj #	Name	Description	Comments/Financial	BOARD SUB COMMITTEE SORT	Contract/Technical Information		
С	New High School	School development		1	Projects C/D might be combined (same campus)		
L	Collins Portable Demo	Removal of portables		2			
Α	9th Grade School renovation	Modernization project/face lift		3			
D	СТЕ	School development		4			
В	District wide technology	Network upgrade - Outdoor Wi-Fi - 1:1 Initiative		5			
F	Infrastructure Replacement	Utilities upgrades		6			
Н	Tanner	Covered walkways		7			
S	Renovate student restrooms / drinking fountains			8			
N	Portable Replacements	District wide portable replacement		9			
U	Modernize oldest K-5 sites	Improve media centers / admin buildings		10			
К	Al ondra Shade	Outdoor stage shade structure		11			
E	Traffic drop off/on relief	Collins/Alondra/Keppel/ Wirtz/Mokler traffic mitigation		12			
J	Elementary Retrofits	Modernization projects/face lift		13			
R	Flooding issues, various sites			14			
М	CDS Site Needs	Data needed		15			
Р	Window Replacement	District wide window/frame replacements		16			
Т	Outdoor Activities	To promote physical fitness & structured play		17	Possible City partnership		
G	New Pool	Aquatic center construction		18			
V	Alondra Auditorium/Cafetorium	No current large venue		19			
0	Track - Alondra	New track development		20			
Q	District as phalt	Parking renovation at District Office		21			
-1	WroughtIron	Fencing replacement - Hold		22			


Other projects:

- District has replaced over 55 HVAC units over summer
- LED exterior lighting replacement project completed, now working on interior LED lighting replacement

• NEXT STEPS:

- Odyssey design and phases
- Portable DSA approvals
- H2O dispenser deployment





The mission of the Paramount Unified School District is to ensure learning and success for each student by providing a quality education.

